

Digital Gift Card Loyalty Exchange (DGCLPE)


Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Name: Prathamesh Kumar Singh

SRN: PES1UG24CS341

Section: 5F

Screenshot 1: Backlog with Epics and User Stories

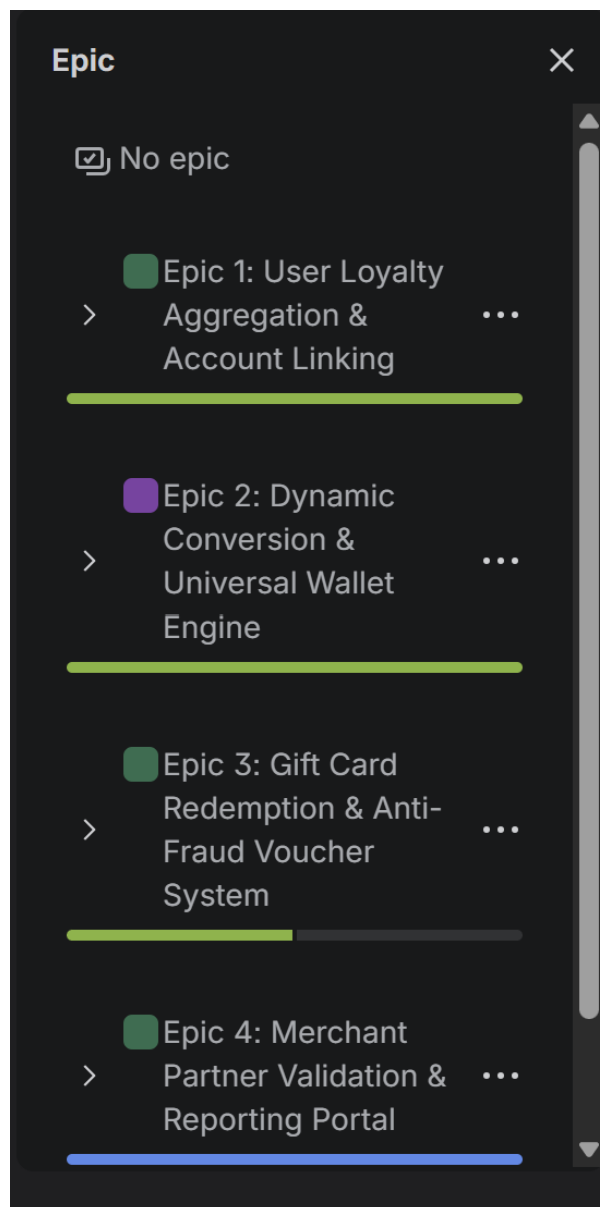

Screenshot 2: Story Point Assignments

▼

DGCLPE Sprint 2

5 Sep – 12 Sep (6 work items)

8

13

6

Complete sprint

...

DGCLPE-8

1.4 Manually Sync/Refresh ...

Epic 1: User Loyalt...

Done

3

=

DGCLPE-11

2.3 View Universal Credit ...

Epic 2: Dynamic C...

Done

3

=

DGCLPE-17

4.2 View Conversion Stati...

Epic 4: Merchant P...

In Progress

5

=

DGCLPE-16

4.1 Validate Redeemed Vo...

Epic 4: Merchant P...

In Progress

8

=

DGCLPE-14

3.3 Cryptographic Vouche...

Epic 3: Gift Card R...

To Do

5

>

DGCLPE-15

3.4 View Redeemed Vouc...

Epic 3: Gift Card R...

To Do

3

=

▼

Backlog

(0 work items)

0

0

0

Create sprint

Your backlog is empty.

Screenshot 3: Active Sprint View

TO DO 2

3.3 Cryptographic Voucher Locking

Epic 3: Gift Card Redemption & Anti-Fraud Voucher ...

DGCLPE-14

5

>

3.4 View Redeemed Voucher Status

Epic 3: Gift Card Redemption & Anti-Fraud Voucher ...

DGCLPE-15

3

=

+ Create

IN PROGRESS 2

4.2 View Conversion Statistics

Epic 4: Merchant Partner Validation & Reporting Por...

DGCLPE-17

5

=

4.1 Validate Redeemed Voucher

Epic 4: Merchant Partner Validation & Reporting Por...

DGCLPE-16

8

=

DONE 2

1.4 Manually Sync/Refresh Merchant Points

Epic 1: User Loyalty Aggregation & Account Linking

DGCLPE-8

3

=

2.3 View Universal Credit Balance

Epic 2: Dynamic Conversion & Universal Wallet Engi...

DGCLPE-11

3

=

Screenshot 4: Burndown Chart



Reflection Questions

1. Did your estimations reflect the actual effort?

Our team used Planning Poker with the Fibonacci sequence to assign story points. The 8-point stories (such as Story 2.2 - Convert Points to Universal Credits and Story 3.2 - Redeem Credits for Gift Card) represented significant complexity due to dynamic rate calculations and external API integrations. The 2-point stories were simple UI lists, such as viewing merchant partners. In our simulation, we completed all stories within both sprints, suggesting our estimates were reasonable. However, Story 3.3 (Cryptographic Voucher Locking) with 5 points might have been slightly underestimated, as cryptographic implementation typically requires additional security review and testing. Overall, the estimation process was effective, and the Fibonacci scale provided a good framework for relative sizing.

2. Was your backlog well-prioritized?

Yes, our backlog was well-prioritized based on business value and user needs. We placed the core user journey first – Epic 1 (Account Linking) and Epic 2 (Conversion) were top priority because users cannot redeem anything without first connecting accounts and converting points. Epic 3 (Redemption) came next because it represents the primary value proposition for users. Epic 4 (Merchant Portal) was placed at Medium priority since merchants need validated data after users start redeeming. Within each Epic, stories with "High" priority were placed first, while supporting features like manual sync (Story 1.4) and viewing redemption status (Story 3.4) were correctly placed in Sprint 2. This prioritization ensured that the Minimum Viable Product (MVP) could be delivered in Sprint 1.

3. How did your simulated sprint align with your plan?

Sprint 1 was planned with 7 stories totaling 32 story points, covering the entire user journey from linking accounts to redeeming a gift card. We successfully moved all stories across the workflow (To

Do → In Progress → Done) within the 1-week simulation. The simulation showed that our planned capacity of approximately 30 points per sprint is realistic for this project. Sprint 2 had 6 stories totaling 27 points and was also completed successfully. One insight from the simulation was that complex stories (8 points) should be started earlier in the sprint to allow time for unexpected issues. Overall, the simulation aligned well with our plan, and we delivered all committed scope by the end of each sprint.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart for Sprint 2 shows a steep decline on the first day, followed by a flat line at zero for the remaining days. This occurred because, during the simulation, we batched the movement of tasks across the workflow in one session. While the chart does not show a gradual daily decline, it successfully demonstrates that all 27 story points were completed by the end of the sprint, and the red line ends at zero, indicating full scope delivery. In a real project, this pattern could indicate that stories were not broken down into smaller tasks or that work was completed in large batches. Moving forward, we would break larger stories (8 points) into smaller sub-tasks and spread work more evenly across the sprint days to achieve a smoother burndown. The chart also confirms our sustainable velocity is approximately 25-30 points per sprint, which we will use for future sprint planning.
